



2024 Street Improvement Project Construction Update #7

Current Events

The Contractor has completed paving the first layer of asphalt along Roosevelt Ave NE north of 33rd Ave NE and portions of 34th Ave NE and 35th Ave NE this week (week of July 22nd). The Contractor has also begun adjustment sewer castings and gate valves to all roadways north of 33rd Ave NE and will continue these adjustments on Saturday, July 27th, along with patching curb replacement locations.

The City of St. Anthony allows work on Saturdays from 9AM to 7PM.

The Contractor has begun removal and replacement of deficient curb in areas south of 33rd Ave NE this week and will continue next week (week of July 29th).

See reverse for project location map.

Future Events

The Contractor is anticipated to begin paving roadways north of 33rd on Thursday, August 1st.

The Contractor is anticipated to patch curb replacement areas later in the week (week of July 29th).

Please note: The roadways will remain open to traffic throughout the project; however, parking along the roadway will be restricted to allow for the replacement of curb.

The Contractor has tentatively scheduled the removal and replacement of deficient sidewalk within Salo Park in August and the trail and parking lot improvements within Silver Point Park in September.

The above schedule is tentative and is subject to change due to weather or scheduling conflicts.

Roadway Paving

Following paving of your roadway:

- Do not turn your wheels at a stop condition on a newly paved road to avoid leaving impressions in the pavement.
- As soon as the rollers have made a couple of passes on the fresh asphalt you may drive on it.

Lawn Irrigation and Pet Fences

If you have a lawn irrigation system or pet fence within the City right-of-way, please mark the location of the sprinkler heads before construction. This will allow the contractor to take precautionary measures to protect your irrigation system and pet fence or identify where to replace the system if it cannot be avoided.

Tips of the Week

- Please observe posted detour and warning signs.
- Slow down and watch for uneven surfaces.
- Stay alert! Watch for signs, equipment, and workers.
- Please remind children to stay away from the construction site, equipment, and stockpiles of materials.
- Access through the site may change throughout the day as construction progresses; your patience is appreciated.


Project Contacts

Onsite Project Representative: Kate Achenbach (651) 302-3367

Project Manager: Katie Koscielak (612) 282-3641

City Engineer: Justin Messner (612) 388-9652

Director of Public Works: Jeremy Gumke (612) 782-3441

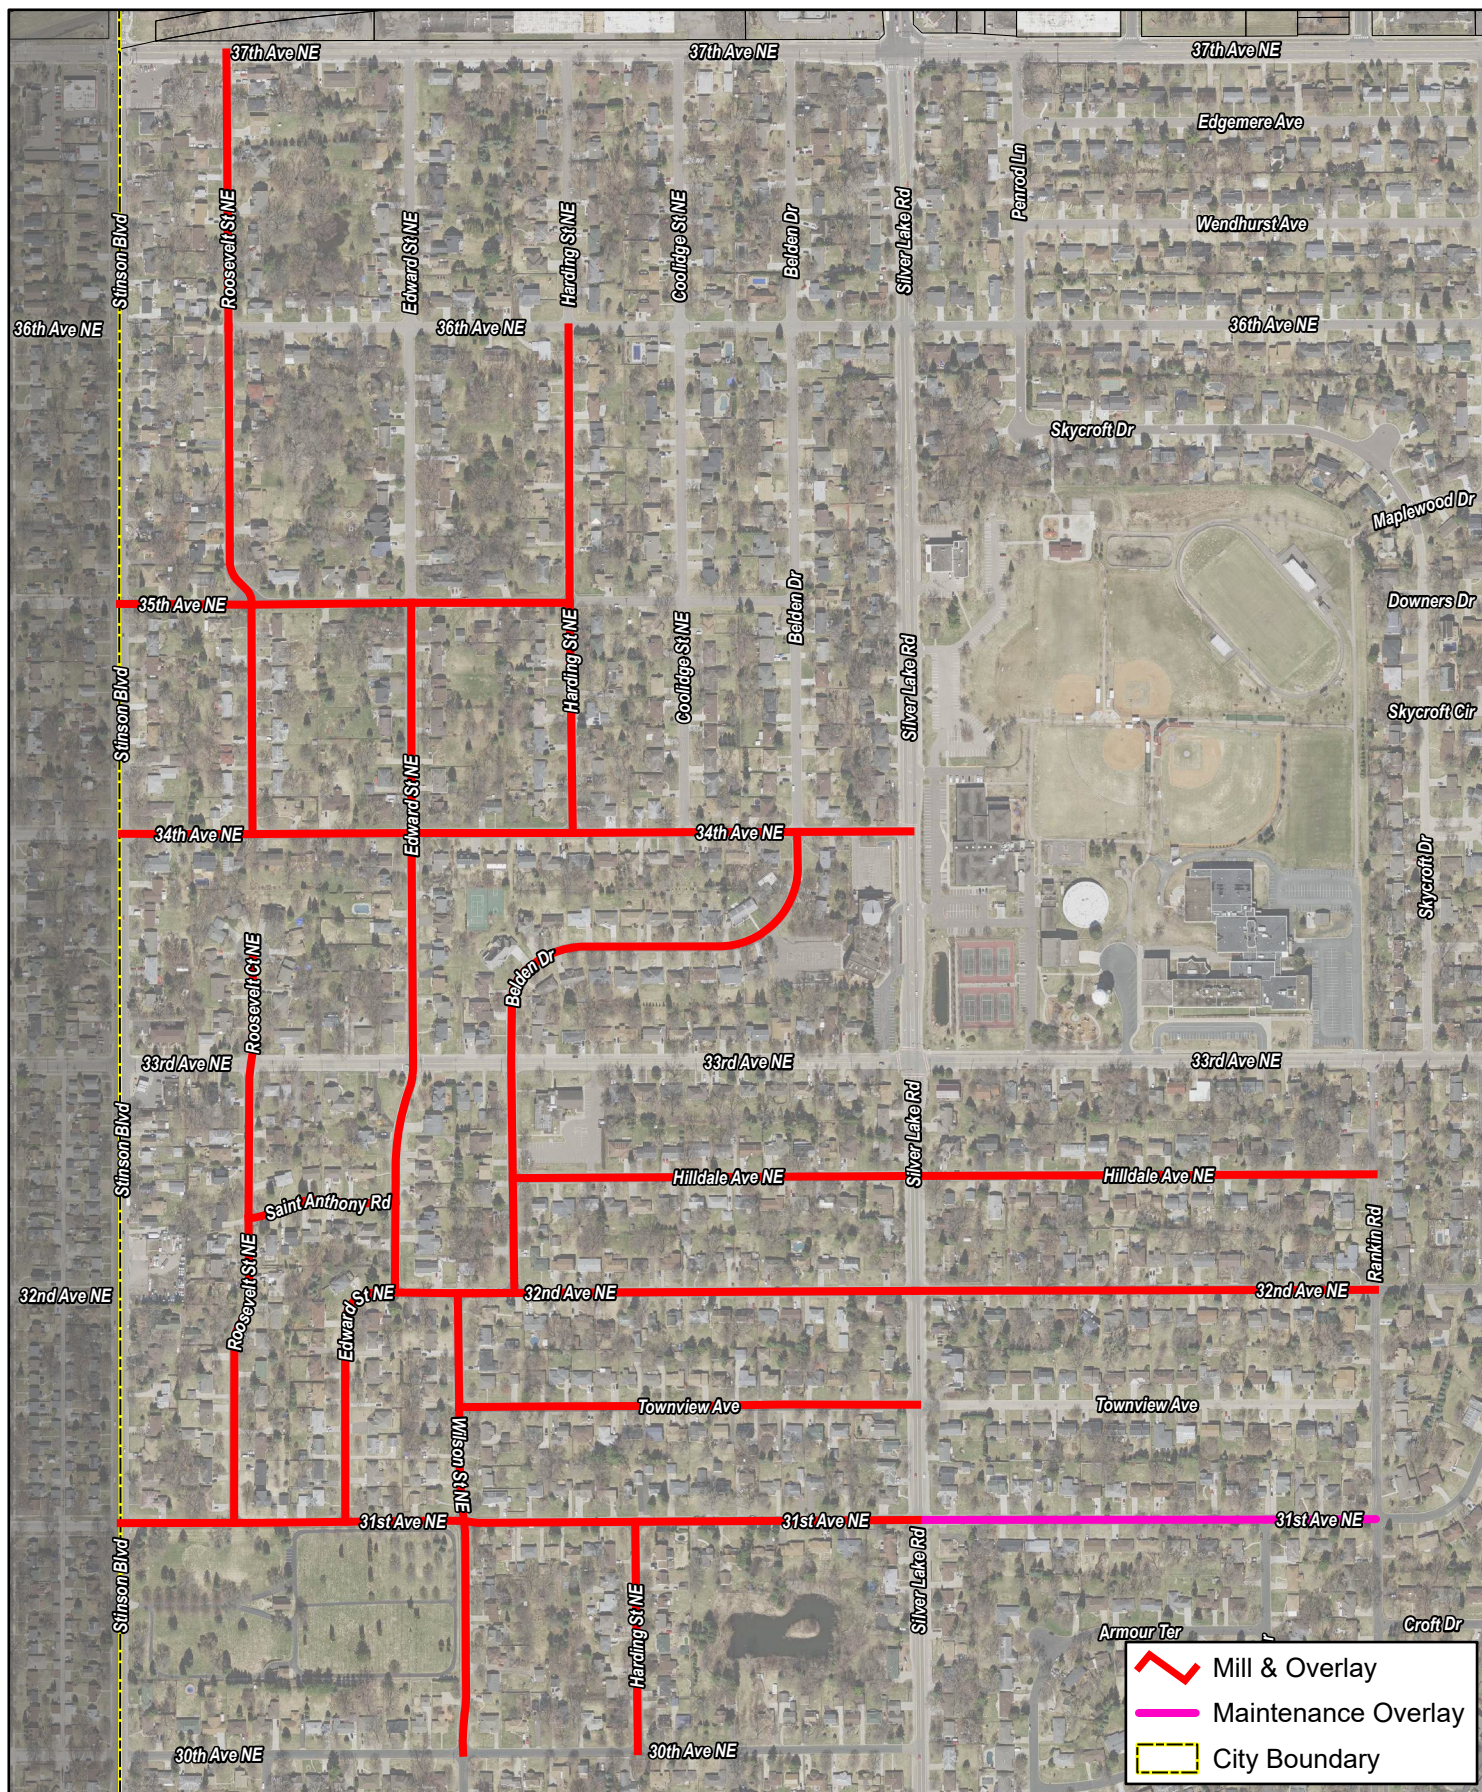

2024 STREET IMPROVEMENT PROJECT
FIGURE 1 - LOCATION MAP
ST. ANTHONY VILLAGE, MINNESOTA

