



2016 Street and Utility Improvement Project



Stinson Boulevard

Project Schedule Update

The Contractor is anticipated to complete all utility installations by end of day Friday, June 10th, with the exception of the water main to be bored under the railroad tracks, **weather permitting**.

The following is an anticipated schedule of upcoming construction activities:

June 13—June 17

- Continue building the road section from 40th Avenue and continuing south (including drain tile and class 5 installation).
- Begin boring new water main under the railroad tracks. **Boring of the water main will require access to Stinson Boulevard from 37th Avenue to be restricted until boring operations have been completed.**
- Begin concrete curb and gutter installation between Silver Lane and 39th Avenue.

June 20—June 24

- Continue building road section south of 40th Avenue (including drain tile and class 5 installation).
- Finish boring new water main under the railroad tracks.
- Begin concrete curb and gutter installation between 39th Avenue and 37th Avenue.

June 27—July 1

- Base course paving. The road will be reduced to one lane during paving operations. Traffic will be allowed to travel on the new surface within a few hours after the pavement has been placed. Please be on the look out for road detours.

Thank you for your continued patience

As we continue the street and utility reconstruction, please be aware that construction activities are noisy, dusty, and very inconvenient. The project team will do their best to complete the project in a timely fashion and to minimize the disturbances to you and your property. Please be patient and if you have questions do not hesitate, call us!

Questions?

If you have any questions or concerns, Justin Moeller is the quickest way to receive answers to your questions. If Justin Moeller is unavailable, please call Justin Messner at the number provided below.

Changes to Construction Schedule

Please be aware the construction schedule may change throughout the project as a result of weather conditions or other activities beyond the contractor's control. Should a major change in the schedule be anticipated, we will do our best to communicate the change through this newsletter and through your field contact, Justin Moeller.

Paving

Paving of the roadway will limit access to properties and restrict through traffic access during construction working hours.

June 10, 2016

Project Contacts

Justin Moeller
Onsite Project Rep
(612) 360-9908

Justin Messner
Project Manager /
Business Liaison
(612) 388-9652

Todd Hubmer
St. Anthony City Engineer
(763) 287-7182

Jay Hartman
St. Anthony Director of
Public Works
(612) 782-3314



Kevin Hansen
Columbia Heights
City Engineer / Director of
Public Works
(763) 706-3700

Additional Information and Tips:

- Please observe posted detour and warning signs.
- Please do not park vehicles on streets under construction.
- Slow down and watch for uneven surfaces.
- Stay alert! Watch for signs, equipment, and workers.
- Please remind children to stay away from the construction site, equipment, and stockpiles of materials.
- Access through the site may change throughout the day as construction progresses, your patience is appreciated.



2016 Street & Utility Improvements

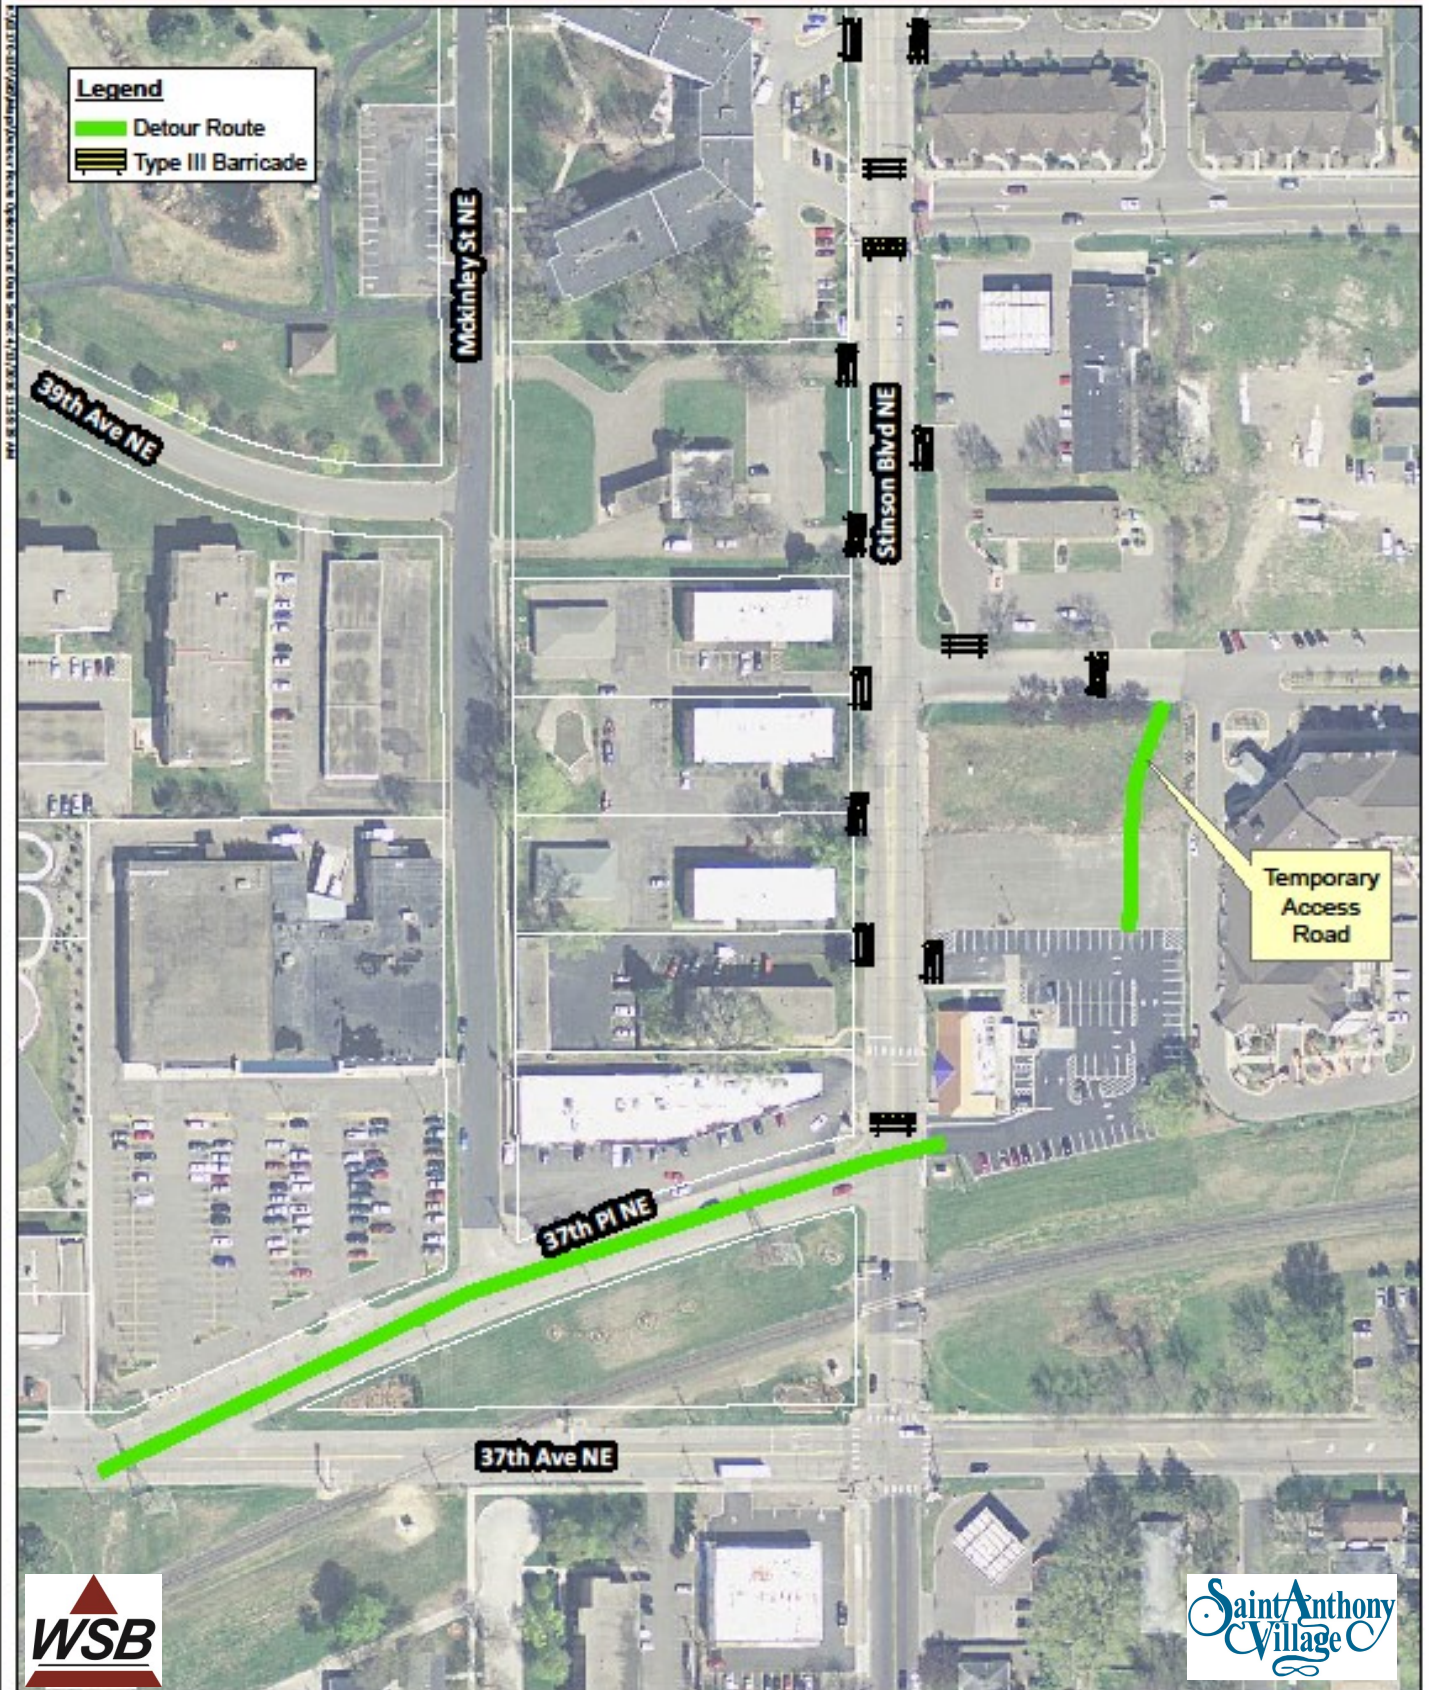

Project Location
St. Anthony, MN

