



2016 Street and Utility Improvement Project



Stinson Boulevard

Project Schedule Update

The week of April 11th, Stinson Blvd was closed between 37th Place and Silver Lane. Traffic control has been the project team's top priority. Additional signage and detours have been added as needed to control and reroute traffic. Crews are working to install temporary driveway access to local businesses and residences. The attached maps indicate the detour routes and temporary driveway accesses.

CenterPoint Energy will begin gas main and service replacement the week of April 18 starting at the intersection of Stinson Blvd and Silver Ln and continuing south .

The following is an anticipated schedule of upcoming construction activities:

April 18—April 22

- Pavement removal between 38th Ave and Silver Ln.
- Installation of temporary water.
- Begin replacing sanitary sewer, water main, and storm sewer at the intersection of Stinson Blvd and Silver Ln.

April 25—April 29

- Continue sanitary and storm sewer installation from Silver Ln to the south.

May 2—May 6

- Complete sanitary and storm sewer installation between Silver Ln and 3900 Stinson Blvd.
- Begin trunk storm sewer replacement from 3900 Stinson Blvd to the south.

The Stinson Blvd/Silver Ln intersection is anticipated to be closed to thru traffic through May 6. A traffic detour will be posted throughout the road closure rerouting traffic onto Silver Lake Rd and 37th Ave NE.

Bus Service

Metro Transit has been notified of the project schedule and has posted the temporary bus routes for the duration of the project at the existing bus stops along the project corridor.

The local school bus service and Metro Transit have been made aware of the anticipated closure at Stinson Blvd and Silver Ln and accommodations are being made for students and commuters during this closure.

Changes to Construction Schedule

Please be aware the construction schedule may change throughout the project as a result of weather conditions or other activities beyond the contractor's control. Should a major change in the schedule be anticipated, we will do our best to communicate the change through this newsletter and through your field contact, Justin Moeller.

Questions?

If you have any questions or concerns, Justin Moeller is the quickest way to receive answers to your questions. If Justin Moeller is unavailable, please call Justin Messner at the number provided below.

Thank you for your continued patience

As we continue the street and utility reconstruction, please be aware that construction activities are noisy, dusty, and very inconvenient. The project team will do their best to complete the project in a timely fashion and to minimize the disturbances to you and your property. Please be patient and if you have questions do not hesitate, call us!

April 15, 2016

Project Contacts

Justin Moeller
Onsite Project Rep
(612) 360-9908

Justin Messner
*Project Manager /
Business Liaison*
(612) 388-9652

Todd Hubmer
St. Anthony City Engineer
(763) 287-7182

Jay Hartman
St. Anthony Director of Public Works
(612) 782-3314

Kevin Hansen
*Columbia Heights
City Engineer / Director of
Public Works*
(763) 706-3700

2016 Street & Utility Improvements

K:\02170-130\GIS\Map3\Detour Route Option 2.mxd Date Saved: 4/13/2016 11:58:42 AM

Legend

- Detour Route
- Type III Barricade

Mckinley St NE

39th Ave NE

Stinson Blvd NE

Temporary
Access
Road

37th Pl NE

37th Ave NE




0 100 200 Feet

Project Location
St. Anthony, MN



2016 Street & Utility Improvements

K:\02170-130\GIS\Map3\Detour Route Option 3.mxd Date Saved: 4/13/2016 11:57:29 AM

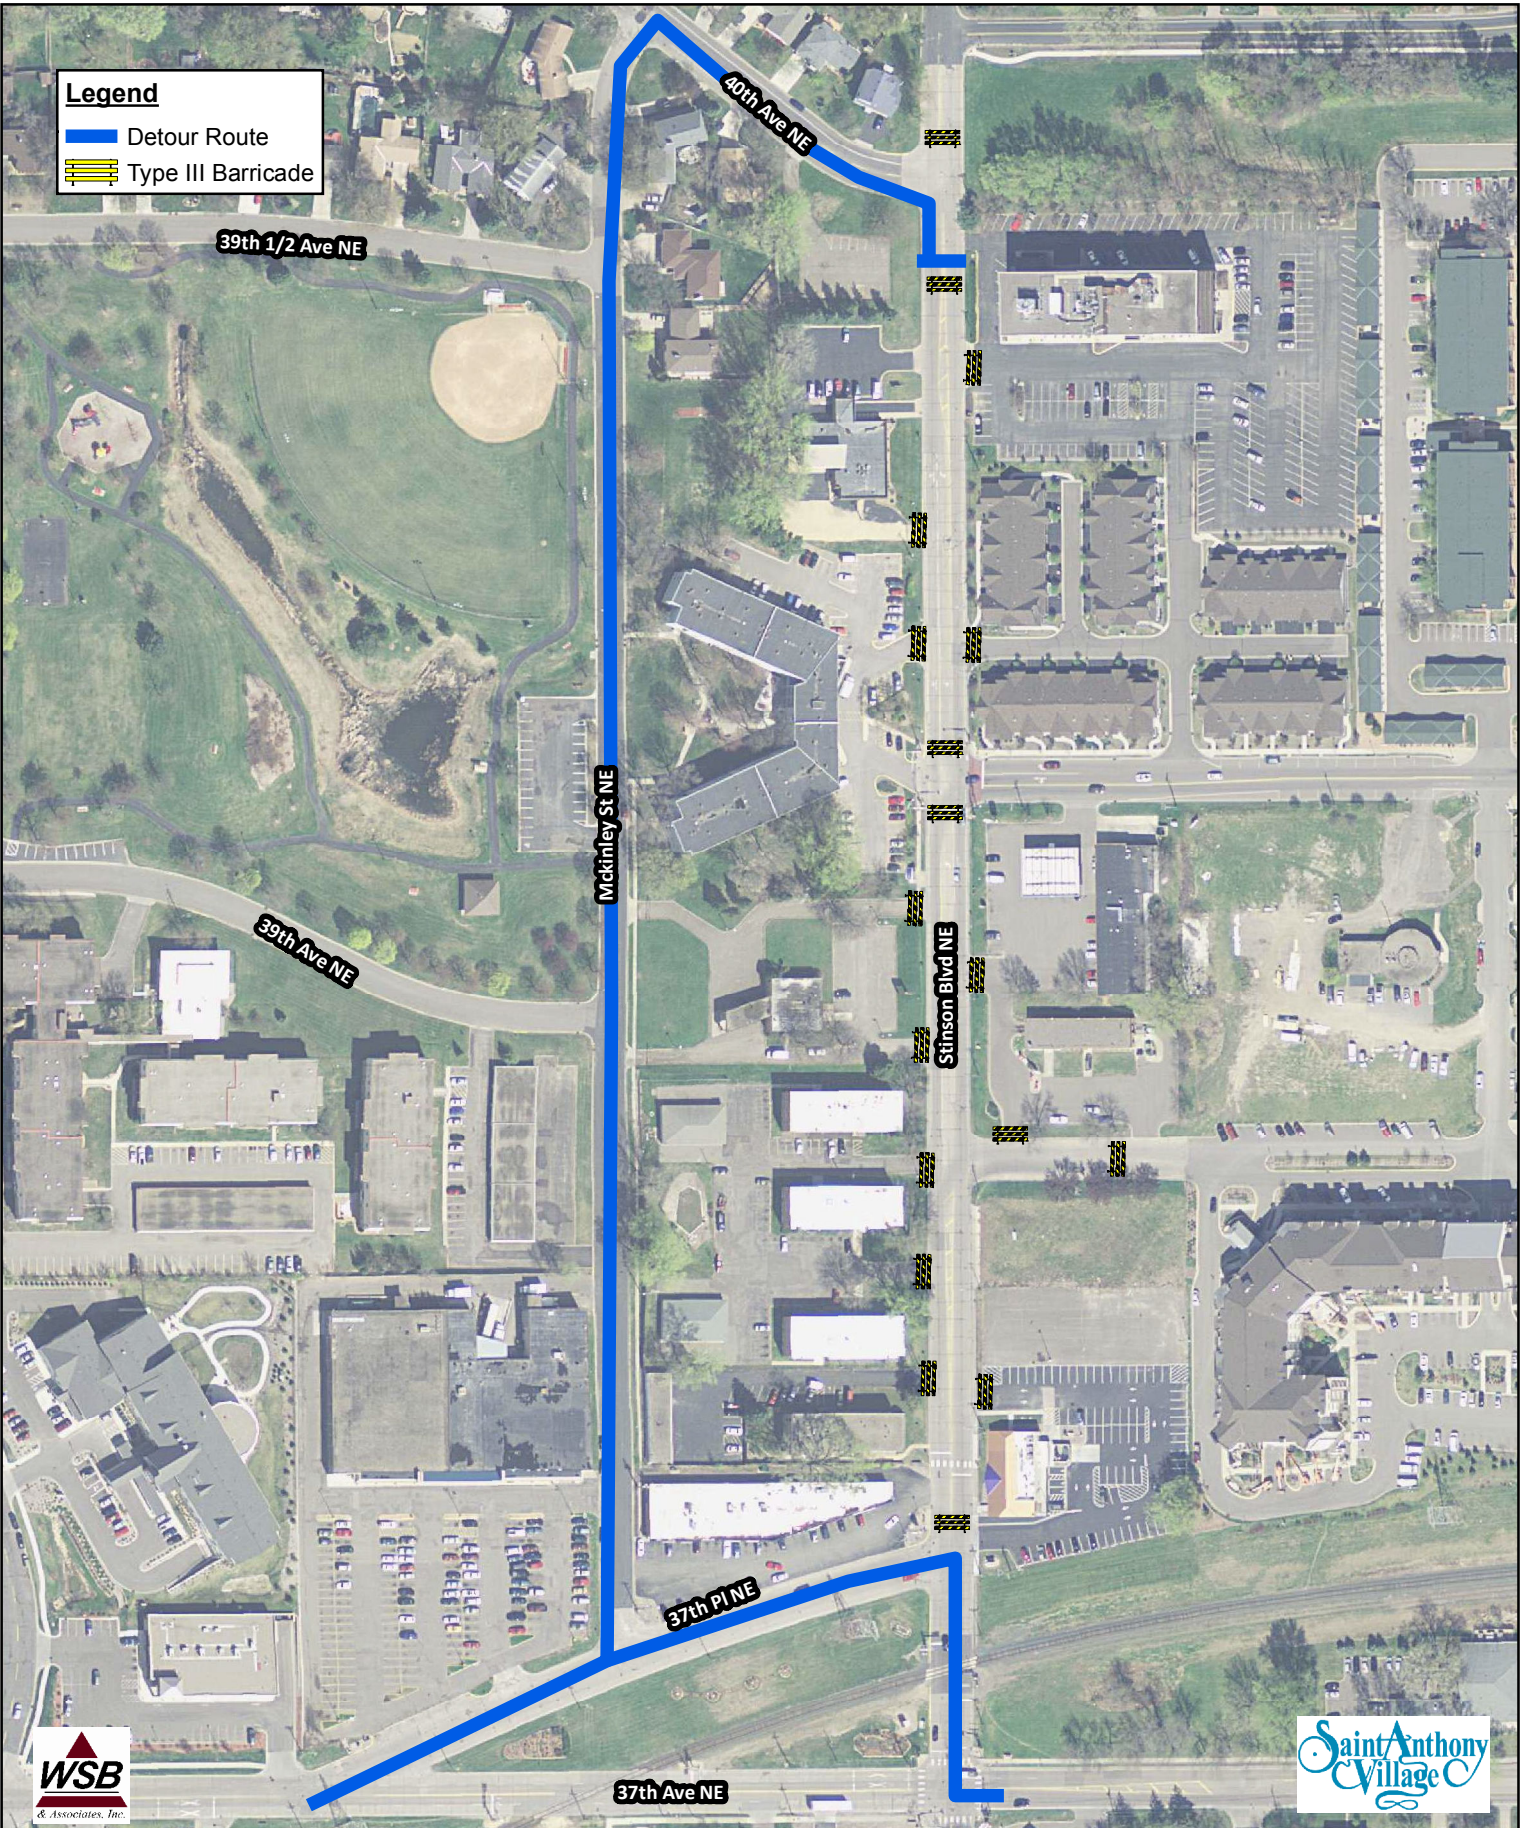

0 100 200
Feet

Project Location
St. Anthony, MN

